

5. Project Schedule

5.1 Work Breakdown Structure (WBS)

Our WBS if FoodNest project we have distributed in 6 phases, 29 tasks and 9 milestones/deliverables across in 14-week timeline. And Each task is assigned to a responsible team member that includes the duration in working days, predecessor dependencies and classification as a milestone or deliverable where it is applicable.

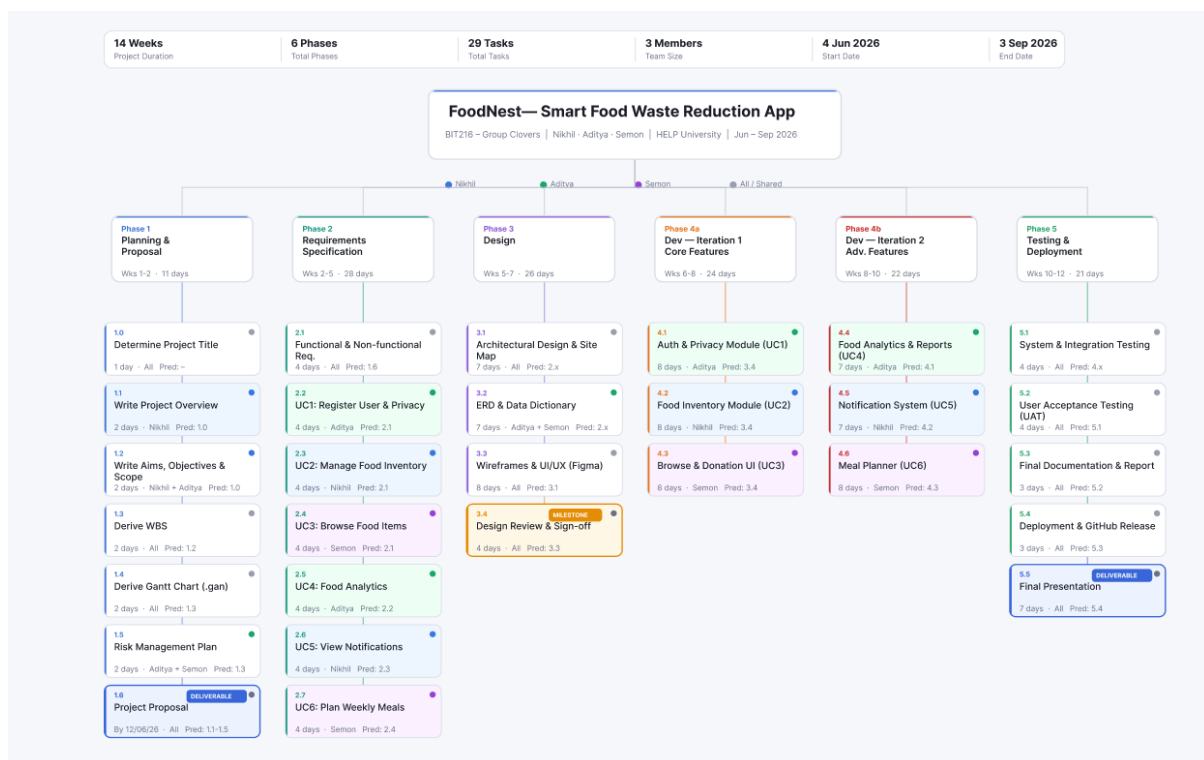


Figure 1: WBS Diagram

Phase 1 – Planning & Proposal (Weeks 1-2, 11 days):

- The project foundations will include scope, objectives, team members structure and planning of artifacts.
- Task Distribution and Discussion: Project Overview, write aims, Objectives and Scopes, Derive WBS, Derive of Grantt Chartt, and Risk Management Plan.
- Deliverables: 1.6 Project Proposal submitted 12 Jun 2026. Lead by Nikhil.

Phase 2 – Requirements (Weeks 2-5, 28 days):

- Documentation of all functional and non-functional requirements with the dedicated use case specifications for each of the 6 core features.
- Task: All Functional and Non-Functional Requirements, Use Case 1 – 6 specifications.
- Task Distribution: Aditya (UC1, UC4), Nikhil (UC2, UC5) and Semon (UC3, UC6).

Phase 3 – Design (Weeks 5-7, 26 days):

- It will cover all the system and UI/UX design before development begins.
- Task: Architectural Design and Site Mapping, ER Diagram and Data Dictionary, Wireframes and UI/UX in Figma.
- Milestones: 3.4 Design Review and Sign off. Internal checkpoints before any coding phase starts.
- Task Distributions: All members as Aditya and Semon will be leading ERD.

Phase 4a – Development: Core Features (Weeks 6-8, 24 days):

- We will start First Development Sprint where all three main features start at same time.
- Task: Auth and Privacy Module (Use Case 1), Food Inventory Modules (Use Case 2), and Browse and Donation UI (Use Case 3).
- Task Distribution: Aditya (Use Case 4), Nikhil (Use Case 2), and Semon (Use Case 3).

Phase 4b – Development: Advance Features (Weeks 8-10, 22 days):

- Second Development sprint will be starting where three advance use cases on will begin for top of the core system.
- Task: Food Analytics and Report (Use Case 4), Notification System (Use Case 5) and Meal Planner (Use Case 6).
- Task Distribution: Aditya (Use Case 4), Nikhil (Use Case 5), Semon (Use Case 6).

Phase 5 – Testing and Deployment (Weeks 10-12, 21 days):

- Team will validate full system, and team will prepare for final submissions.
- Task: System and Integration Testing. User Acceptance Testing, Final Documentation and Deployment & GitHub release.
- Deliverable: 5.5 Final Presentation.
- Team Distribution: All members.

Team Roles and Color Coding:

Member	Roles	Color
Nikhil Rana	Team Leader, Project Planning, UC2 and UC5.	Blue
Aditya Kumar Jaiswal	Requirements, UC1, UC4.	Green
Semon Chakhradhar	UC3, UC6, ERD	Purple
All	Collaborative tasks	White

5.2 Milestones & Deliverables




Figure 2: Milestone and Deliverables

Here is the Milestone and Deliverables table:

#	Types	Name	Date
M1	DELIVERABLES	Project Proposal and Plan	12 Jun 2026
M2	DELIVERABLES	Gantt Chart	12 Jun 2026
M3	DELIVERABLES	Risk Management Plan	12 Jun 2026
M4	DELIVERABLES	Requirements Specification Docs.	26 Jun 2026
M5	MILESTONES	Design (Wireframe and ERD)	16 Jul 2026
M6	MILESTONES	Iteration 1	28 Jul 2026
M7	MILESTONES	Iteration 2	13 Aug 2026
M8	DELIVERABLES	Final Deployment and GitHub Release	27 Aug 2026
M9	DELIVERABLES	Final Presentation	3 Sep 2026

5.3 Gantt Chart

The Gantt Chart was created using application named Gantt Project version 3.3. We chose this application because it captures all phases, tasks, predecessors, resource allocations, and milestones dates for the FoodNest Project. This Gantt chart spans from 4 June 2026 to the month of September 2026 across 14 weeks.

The following screenshot shows the full Gantt Chart view, including all phases, task timelines, and team member allocations:

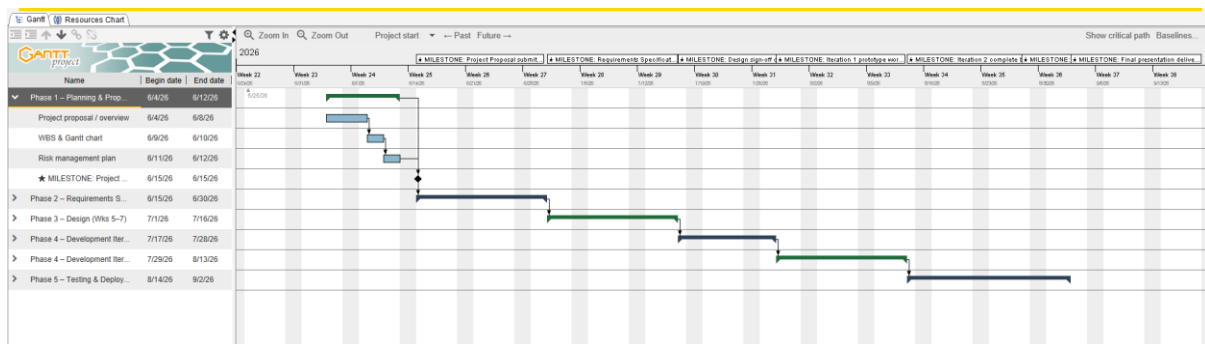


Figure 3: Gantt Chart Phase I

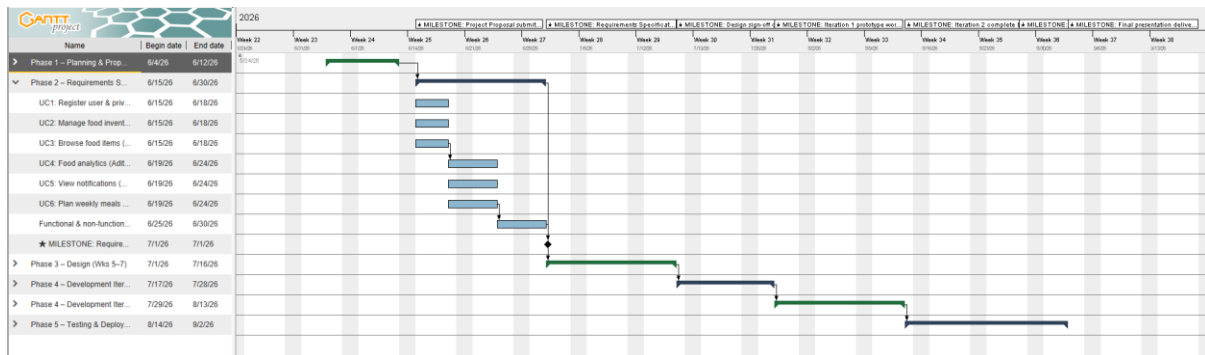


Figure 4: Gantt Chart Phase II

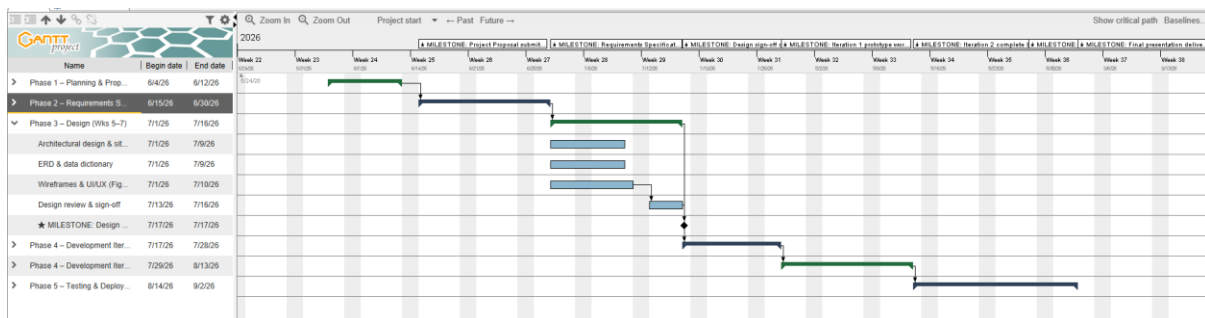


Figure 5: Gantt Chart Phase III

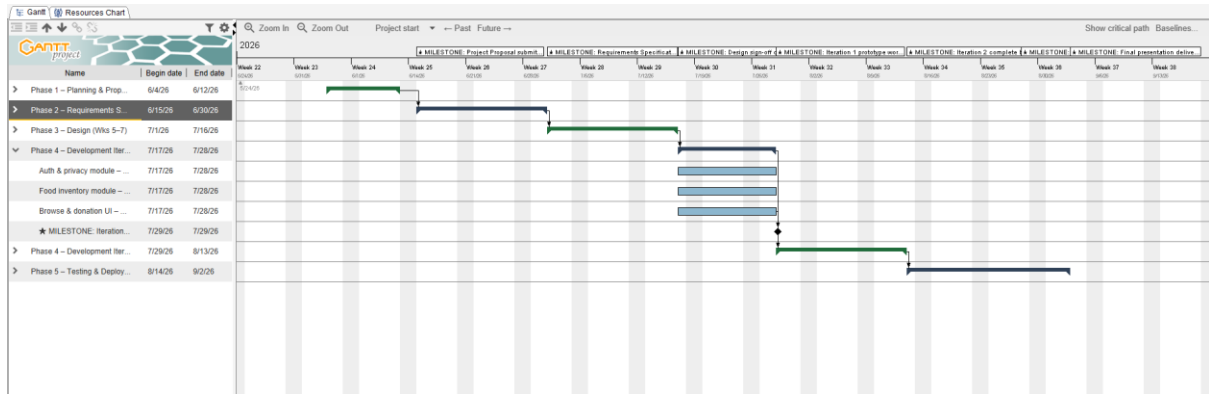


Figure 6: Gantt Chart Phase Iv a

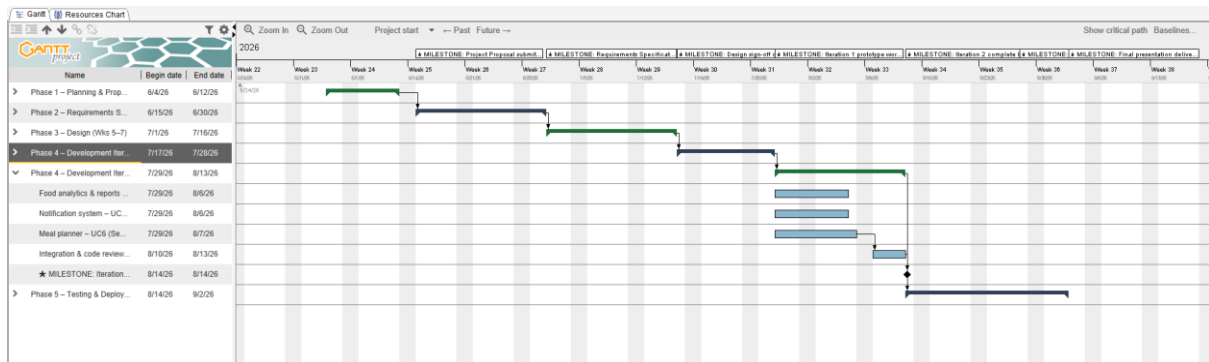


Figure 7: Gantt Chart Phase Iv b

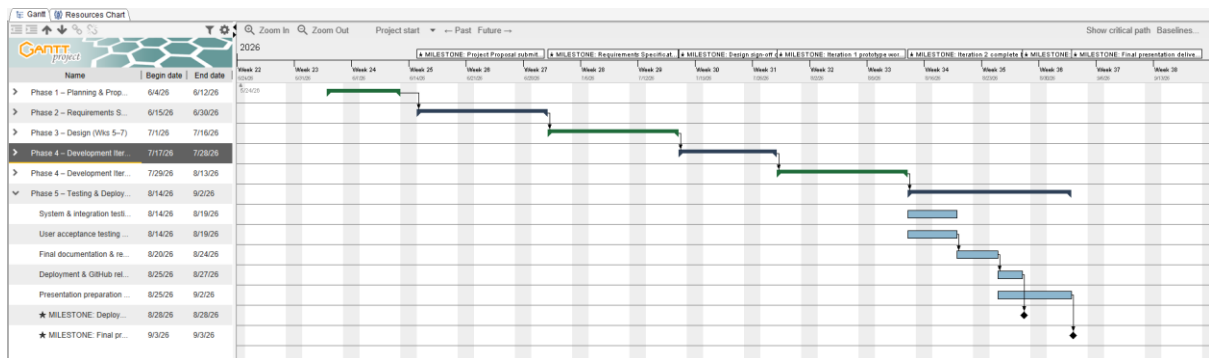


Figure 8: Gantt Chart Phase V

Resource Chart:

Here is the resource chart in Gantt Project that displays the workload distribution across all three team members Nikhil Rana, Aditya Kumar Jaiswal and Semon Chakhradhar. Throughout the project, June to September 2026. And each colored bar will represent the assigned task per member per week.




Figure 9: Resource chart

In figure 9, the cell highlighted in the red indicates week where a team members workload is exceed to 100 percent capacity, and particularly during week 28 – 31 of development in Iteration 1 and 2 where all of the three members are simultaneously working on their respective use case modules and the Cell in blue will represent a normal work load weeks and the chart confirm that each members carries a balanced and comparable overall load across the 14 week project with the peak intensity during the development phase and reduced load during testing and closure phase.

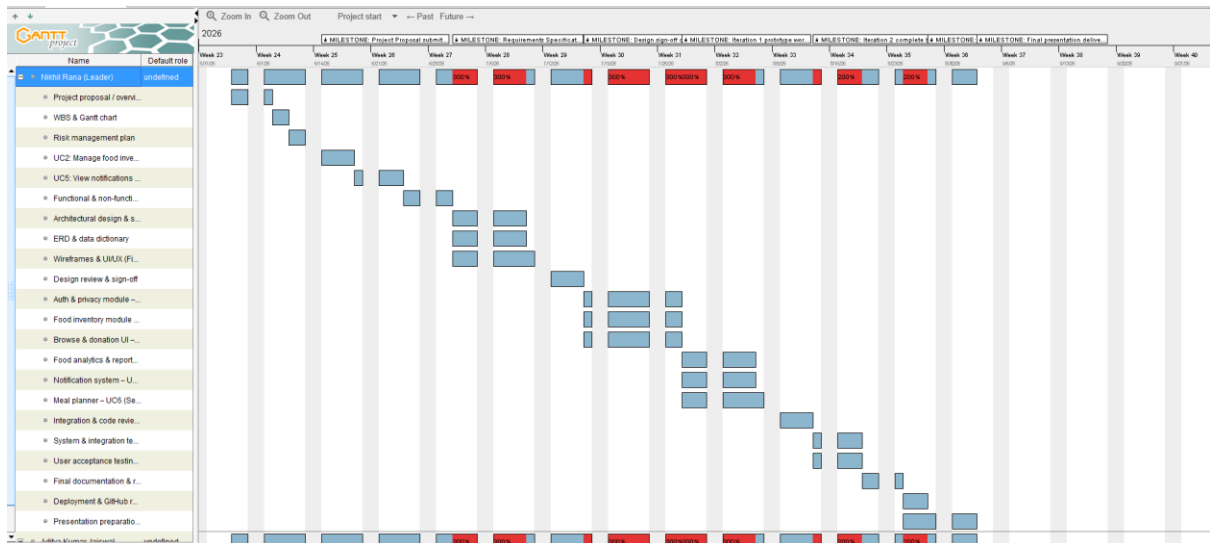


Figure 10: Resource Chart (Nikhil Rana Leader)

This resource chart is for Nikhil Rana where it shows the consistent task allocation across the full 14 week project durations where Nikhil will lead Planning and Proposal phase where it is followed by requirement tasks and contributes to all shared Design and Testing phase.

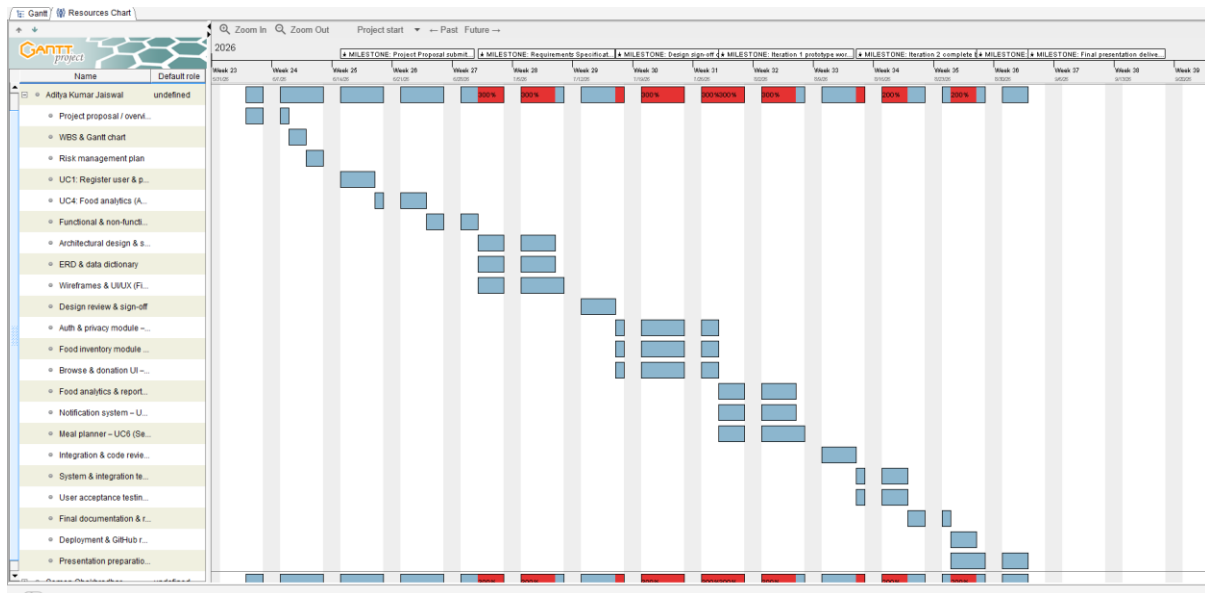


Figure 11: Resource Chart (Aditya Kumar Jaiswal)

This is the resource chart of Aditya Kumar Jaiswal where this chart will reflect active involvement from the early planning phase throughout the whole project closure and his primary ownership covers his UC1 and UC4 along the shared collaboration to Risk Management, Requirements and Design Task.

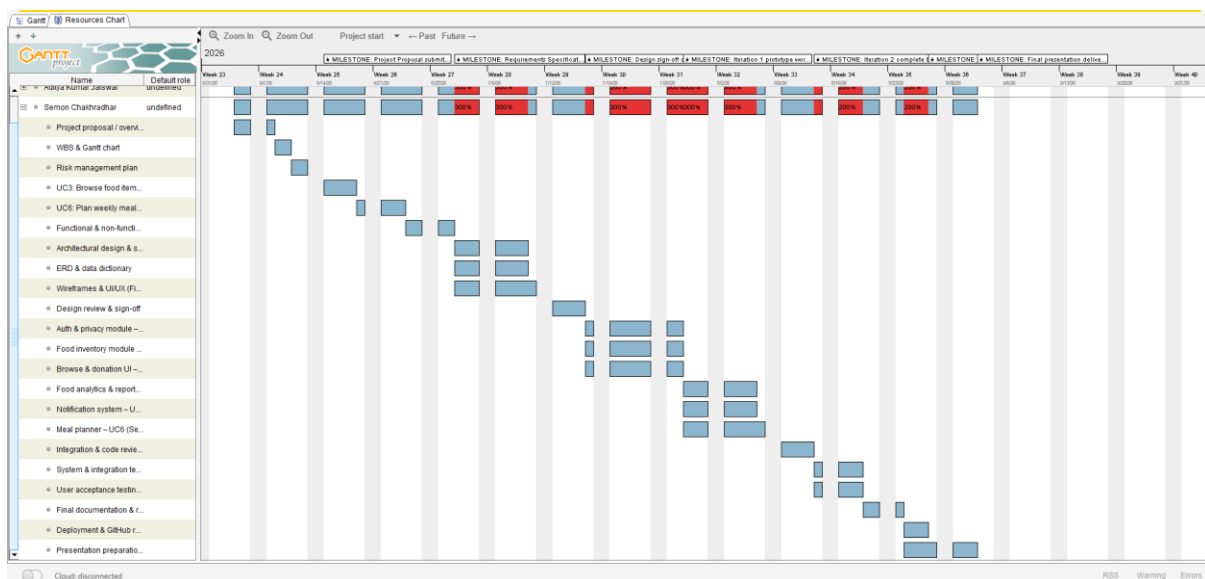


Figure 12: Resource Chart (Semon Chakhradhar)

This is the Semon resource chart which follows the same overall pattern as the team with the early involvement in Planning and Risk Management, primary ownership of UC3 and UC6 and shared responsibility across Design, Integration and Testing phase.

